

November 22, 2016

## Road Reconstruction & Substandard Water Service Replacements on Chapman Road and Arcade Drive Road Resurfacing on Adonis Court

**Contract: 16ECS-TI-104LR**

**Start Date: August 29, 2016**

**Original End Date: December 12, 2016**

**Revised End Date: Spring 2017**

*\*Timeline is subject to change.*


At the end of August, The City of Toronto started to replace the City-owned portion of any substandard water services on Chapman Road and Arcade Drive. This work has been completed. This project also involved resurfacing the road on Adonis Court and reconstructing Chapman Road & Arcade Drive (see map). This work was supposed to be completed by December 12, 2016.

Progress on the project was slowed down because there was a two-month delay in completing the utility locates. Utility Locates are mandatory before any work starts as they identify buried utilities (gas, water, cable, phone) to ensure they remain intact when work starts. The project also stopped work for two weeks to work with Urban Forestry to address concerns with the construction process.

At this time, the road work will resume in Spring 2017, this is because paving work requires consistently warmer and drier weather (+7 degrees), which is harder to guarantee at this time of year.

We recognize that a project of this nature is disruptive to the community and apologize for the inconveniences caused by the delayed end date. A new notice will be issued before work starts in the Spring.

### MAP OF WORK AREA

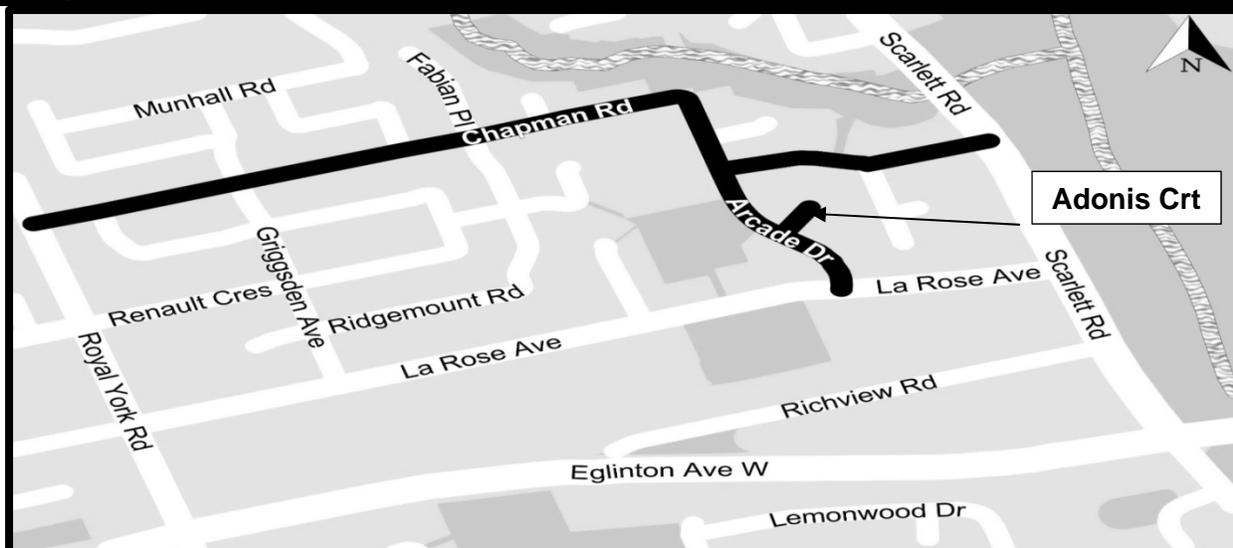

## WORK DETAILS

### To date, the following work has been completed:

- Replacing any substandard water service pipes

### The following work will be completed in the spring 2017:

- Resurfacing the road with new asphalt on Adonis Court
- Reconstructing the road with new granular material and new asphalt on Chapman Road & Arcade Drive



**Restoration:** The construction work area will be restored with sod and/or asphalt where required. Interlocking bricks, flagstone on a granular base, or other similar features that are removed from public and private property during construction will be replaced.

***All restoration work is scheduled for 2017***

## MORE INFORMATION:

If you have questions about the upcoming work, please contact us and quote **Contract 16ECS-104LR**

<b>Field Ambassador</b>	Taras Pawluk, 416-806-1763, taras.pawluk@wspgroup.com
<b>TTY Hearing Impaired Service</b>	416-338-0889 (7 Days a week, 8:00 am – 5:00 pm, closed holidays)
<b>General inquiries</b>	311
<b>Website</b>	<a href="http://toronto.ca/improvements/ward2.htm">toronto.ca/improvements/ward2.htm</a>

Thank you for your patience. Building a great city takes time. Better infrastructure for all of us is worth the wait.
